

2 Aitken Street

Project Update 06

11th September 2017

0%

Progress to date

100%


Project Headlines

- > Precast façade panel removal has been completed adjacent to the St Pauls Apartments and Freyberg Building.
- > Internal strip out of the North-West plant room is nearing completion.
- > Window glazing has been removed where required for precast façade panel removal.

Project look ahead

- > Removal of precast façade panels will continue along Mulgrave street. Processing of the panels will progress in the areas indicated below.
- > Removal of plant from the roof top will commence next week.
- > Deconstruction of the North West plant room will commence this week.
- > Installation of perimeter scaffolding will commence this week to the areas marked below.

Planned works through to mid September:

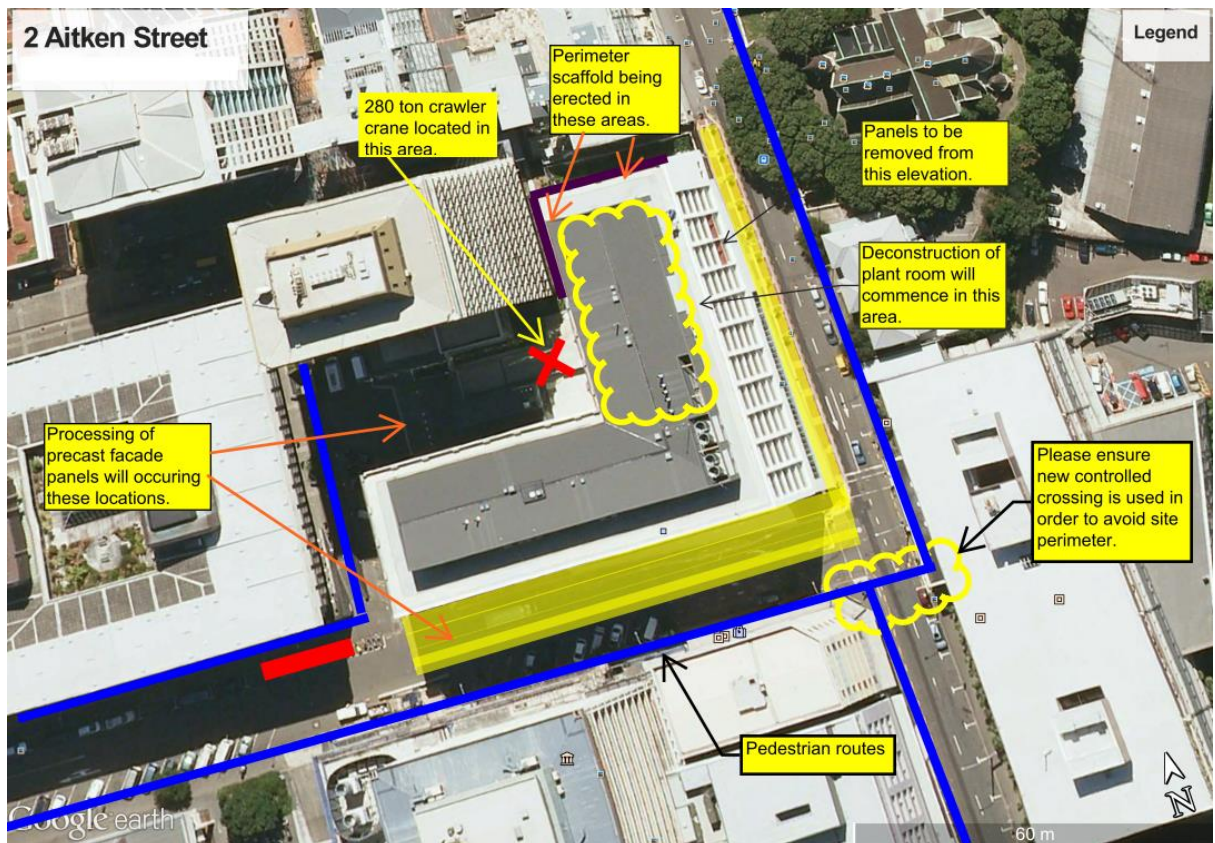

Key Items To Note:

- > While the precast panels are removed from LG-roof on the Mulgrave street elevation, a single lane closure will be in place during off peak times.

Project inquiries

- > Please contact the liaison person for this project within your organisation.
