

2 Aitken Street

Project Update 10

6th November 2017

Progress to date

0%

100%


Project Headlines

- > Cut and crane work is complete on L8 with L7 nearing completion.
- > Removal of the plant rooms has been completed.
- > Roof top panels along Aitken Street have been removed.
- > Internal strip out on level 1 has commenced.

Project look ahead

- > Cut and crane work will continue on L6 & 7 over the next period with the floor units and beam/column joints being broken out ahead of the elements being craned down to the Aitken Street loading bay for processing.
- > Our perimeter scaffold will continue to be reduced in height as the cut and crane work progresses.
- > Further façade panels along Aitken Street are to be removed.
- > Our high reach demolition machinery will be mobilised to site in late November ready to be assembled for the high reach demolition phase of work.

Planned works through to mid November:

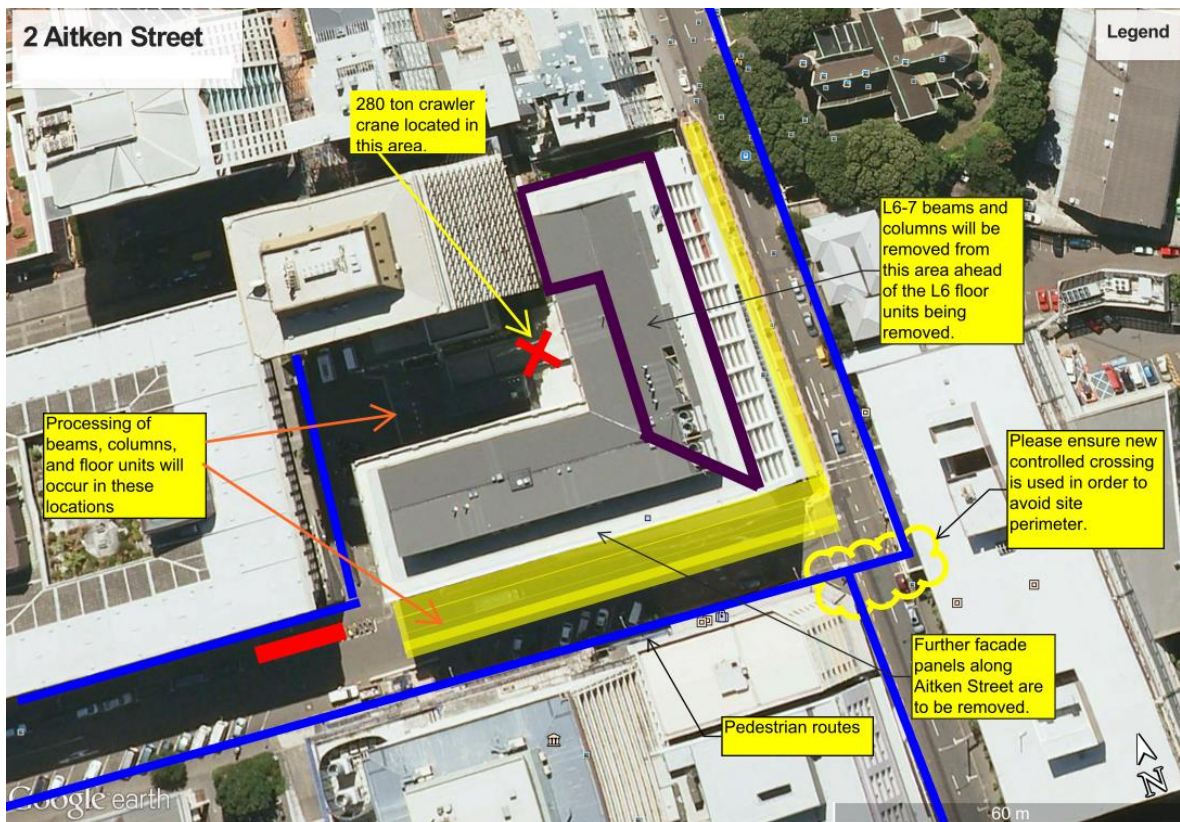

Key Items To Note:

- > As we approach the next phase of work (High reach demolition) on site there will be the following road closures to enable this to occur:
 - > Closure of Aitken Street on Saturday 26th November to enable the high reach demolition equipment to be assembled.
 - > Closure of Aitken Street on Saturday 2nd & Sunday 3rd December to dismantle the 280t crawler crane.
 - > Closure of Aitken Street on Saturday 9th & Sunday 10th December to commence the high reach demolition work.
- > Further detail on these road closures will be provided in the next project update.

Project inquiries

- > Please contact the liaison person for this project within your organisation.
