

PROJECT UPDATE

18th of April 2018


REVERA HOUSE

DEAR NEIGHBOR/BUSINESS OWNER

This an update on the progress of the current deconstruction work happening at the earthquake damaged Revera House.

WORK COMPLETE

RDL Group has completed the soft strip of the entire building including all partition walls, wall linings, windows, timber framing light gauge steel, wire, aluminium, ducting and other metal materials. other stages also completed include consent, scaffolding, enabling works and the deconstruction of the roof, plant room, Lift motor room, Level 10 and Level 9.

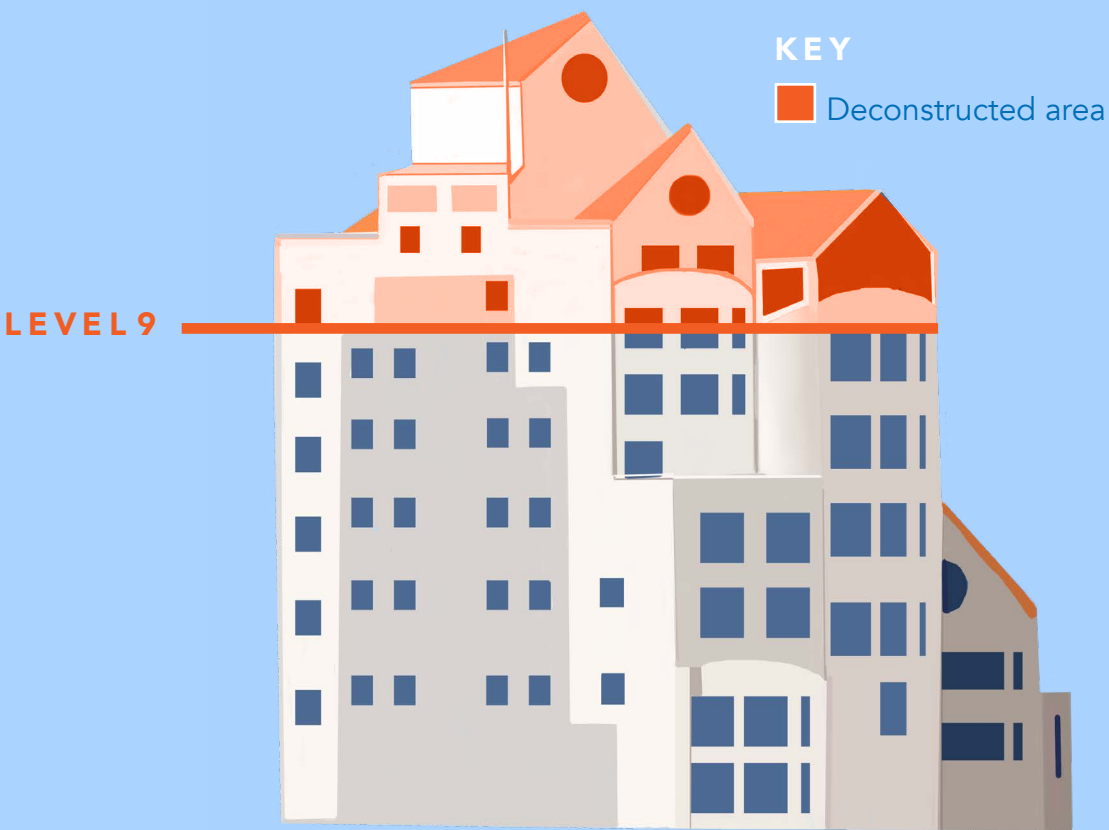

PROGRESS TO DATE

ROAD CLOSURE & TRAFFIC MANAGEMENT

For the reminder of the project the westbound lane of 1-15 Pipitea Street (traffic lights at Murphy/Mulgrave Street, through to Moturoa Street) will be closed between the hours of 6:30 am to 6:00 pm. Appropriate signage and detours will be in place, while we aim to minimise the disruption caused throughout this time there may more noise than usual. we appreciate your patience during this process and apologise in advance for any inconvenience this may cause.

UPCOMING WORKS

- Cut and crane operations will continue on level 9, level 8 and Level 7 over the next period.
- The scaffolding will be lowered in line with the deconstruction.
- The processing, loading, and recycling of materials will continue to be undertaken in the Pipitea Street compound.
- Back propping floors below the current working floors
- Setting up saffoling on Old St. Paul's Church elevation

FUTURE UPDATES

RDL Group will be continuously working closely with all affected parties throughout the duration of this project. We appreciate your patience during this deconstruction period. If you have any further queries about the project, please contact:

0800 RDL GROUP
Emily Fawkner
Emily@rdlgroup.nz

